

PROFESSIONAL SERVICES AGREEMENT

This Professional Services Agreement (“Agreement”) is dated October 19, 2021 (“Effective Date”) and is between the City of Manhattan Beach, a California municipal corporation (“City”) and Ardurra Group, Inc., a Florida corporation (“Consultant”). City and Consultant are sometimes referred to herein as the “Parties”, and individually as a “Party”.

RECITALS

A. City issued Request for Proposals No. E1263-21S on July 26, 2021, titled “Inspection and Construction Management Services for the Polliwog Park Lower Playground Replacement Project”. Consultant submitted a proposal dated August 24, 2021 in response to the RFP.

B. Consultant represents that it is fully qualified to perform such services by virtue of its experience and the training, education and expertise of its principals and employees.

C. City desires to retain Consultant as an independent contractor and Consultant desires to serve City to perform these services in accordance with the terms and conditions of this Agreement.

1. Consultant’s Services.

A. Scope of Services. Consultant shall perform the services described in the Scope of Services (the “Services”) for construction management and inspection services for the Polliwog Park Lower Playground Replacement Project, attached as **Exhibit A**. City may request, in writing, changes in the Scope of Services to be performed. Any changes mutually agreed upon by the Parties, and any increase or decrease in compensation, shall be incorporated by written amendments to this Agreement.

B. Party Representatives. For the purposes of this Agreement, the City Representative shall be the City Manager, or such other person designated in writing by the City Manager (the “City Representative”). For the purposes of this Agreement, the Consultant Representative shall be Dino D’Emilia, Project and Construction Management Group Leader (the “Consultant Representative”). The Consultant Representative shall directly manage Consultant’s Services under this Agreement. Consultant shall not change the Consultant Representative without City’s prior written consent.

C. Time for Performance. Consultant shall commence the Services on the Effective Date and shall perform all Services by the deadline established by the City Representative or, if no deadline is established, with reasonable diligence.

Approved for Use 3/1/2021

D. Standard of Performance. Consultant shall perform all Services under this Agreement in accordance with the standard of care generally exercised by like professionals under similar circumstances and in a manner reasonably satisfactory to City.

E. Personnel. Consultant has, or will secure at its own expense, all personnel required to perform the Services required under this Agreement. All of the Services required under this Agreement shall be performed by Consultant or under its supervision, and all personnel engaged in the work shall be qualified to perform such Services.

F. Compliance with Laws. Consultant shall comply with all applicable federal, state and local laws, ordinances, codes, regulations and requirements.

G. Permits and Licenses. Consultant shall obtain and maintain during the Agreement term all necessary licenses, permits and certificates required by law for the provision of Services under this Agreement, including a business license.

H. Prevailing Wages. This Agreement calls for services that, in whole or in part, constitute “public works” as defined in the California Labor Code. Therefore, as to those services that are “public works”, Consultant shall comply in all respects with all applicable provisions of the California Labor Code, including those set forth in **Exhibit C** hereto.

2. Term of Agreement. The term of this Agreement shall be from the Effective Date through December 31, 2023, unless sooner terminated as provided in Section 12 of this Agreement or extended.

3. Compensation.

A. Compensation. As full compensation for Services satisfactorily rendered, City shall pay Consultant at the hourly rates set forth in the Approved Fee Schedule attached hereto as **Exhibit B**. In no event shall Consultant be paid more than \$294,100.00 (the “Maximum Compensation”) for such Services.

B. Expenses. The amount set forth in paragraph 3.A. above includes reimbursement for all expenditures incurred in the performance of this Agreement.

C. Unauthorized Services and Expenses. City will not pay for any services not specified in the Scope of Services, or reimburse for any expenses not set forth in **Exhibit B**, unless the City Council or the City Representative, if applicable, and the Consultant Representative authorize such services or expenses in writing prior to Consultant’s performance of those services or incurrence of additional expenses. Any additional services authorized by the City Council, or (where authorized) the City Manager shall be compensated at the rates set forth in **Exhibit B**, or, if not specified, at a rate mutually agreed to by the Parties. Any additional expense authorized by the City

Council or (where authorized) the City Manager shall be reimbursed in the amounts authorized by the City Council or City Manager. City shall make payment for additional services and expenses in accordance with Section 4 of this Agreement.

4. Method of Payment.

A. Invoices. Consultant shall submit to City an invoice, on a monthly basis, for the Services performed pursuant to this Agreement. Invoices must be submitted to Anastasia Seims, Senior Civil Engineer, at aseims@manhattanbeach.gov or 3621 Bell Avenue, Manhattan Beach, CA 90266. Each invoice shall itemize the Services rendered during the billing period, hourly rates charged, if applicable, and the amount due. City shall review each invoice and notify Consultant in writing within ten Business days of receipt of any disputed invoice amounts.

B. Payment. City shall pay all undisputed invoice amounts within 30 calendar days after receipt up to the Maximum Compensation set forth in Section 3 of this Agreement. City does not pay interest on past due amounts. City shall not withhold federal payroll, state payroll or other taxes, or other similar deductions, from payments made to Consultant. Notwithstanding the preceding sentence, if Consultant is a nonresident of California, City will withhold the amount required by the Franchise Tax Board pursuant to Revenue and Taxation Code Section 18662 and applicable regulations.

C. Audit of Records. Consultant shall make all records, invoices, time cards, cost control sheets and other records maintained by Consultant in connection with this Agreement available during Consultant's regular working hours to City for review and audit by City.

5. Independent Contractor. Consultant is, and shall at all times remain as to City, a wholly independent contractor. Consultant shall have no power to incur any debt, obligation, or liability on behalf of City. Neither City nor any of its agents shall have control over the conduct of Consultant or any of Consultant's employees, except as set forth in this Agreement. Consultant shall not, at any time, or in any manner, represent that it or any of its officers, agents or employees are in any manner employees of City.

6. Information and Documents.

A. Consultant covenants that all data, reports, documents, discussion, or other information (collectively "Data") developed or received by Consultant or provided for performance of this Agreement are deemed confidential and shall not be disclosed or released by Consultant without prior written authorization by City. City shall grant such authorization if applicable law requires disclosure. Consultant, its officers, employees, agents, or subcontractors shall not without written authorization from the City Manager or unless requested in writing by the City Attorney, voluntarily provide declarations, letters of support, testimony at depositions, response to interrogatories or other information concerning the work performed under this Agreement or relating to

any project or property located within the City. Response to a subpoena or court order shall not be considered "voluntary," provided Consultant gives City notice of such court order or subpoena.

B. Consultant shall promptly notify City should Consultant, its officers, employees, agents or subcontractors be served with any summons, complaint, subpoena, notice of deposition, request for documents, interrogatories, request for admissions or other discovery request, court order or subpoena from any party regarding this Agreement and the work performed thereunder or with respect to any project or property located within the City. City may, but has no obligation to, represent Consultant or be present at any deposition, hearing or similar proceeding. Consultant agrees to cooperate fully with City and to provide City with the opportunity to review any response to discovery requests provided by Consultant. However, City's right to review any such response does not imply or mean the right by City to control, direct or rewrite the response.

C. All Data required to be furnished to City in connection with this Agreement shall become City's property, and City may use all or any portion of the Data submitted by Consultant as City deems appropriate. Upon completion of, or in the event of termination or suspension of this Agreement, all original documents, designs, drawings, maps, models, computer files containing data generated for the Services, surveys, notes, and other documents prepared in the course of providing the Services shall become City's sole property and may be used, reused or otherwise disposed of by City without Consultant's permission. Consultant may take and retain copies of the written products as desired, but the written products shall not be the subject of a copyright application by Consultant.

D. Consultant's covenants under this Section shall survive the expiration or termination of this Agreement.

7. Conflicts of Interest. Consultant and its officers, employees, associates and subcontractors, if any, shall comply with all conflict of interest statutes of the State of California applicable to Consultant's Services under this Agreement, including the Political Reform Act (Gov. Code § 81000, *et seq.*) and Government Code Section 1090. During the term of this Agreement, Consultant may perform similar Services for other clients, but Consultant and its officers, employees, associates and subcontractors shall not, without the City Representative's prior written approval, perform work for another person or entity for whom Consultant is not currently performing work that would require Consultant or one of its officers, employees, associates or subcontractors to abstain from a decision under this Agreement pursuant to a conflict of interest statute. Consultant shall incorporate a clause substantially similar to this Section into any subcontract that Consultant executes in connection with the performance of this Agreement.

8. Indemnification, Hold Harmless, and Duty to Defend.

A. Indemnities.

1) To the fullest extent permitted by law, Consultant shall, at its sole cost and expense, defend, hold harmless and indemnify City and its elected officials, officers, attorneys, agents, employees, designated volunteers, successors, assigns and those City agents serving as independent contractors in the role of City officials (collectively "Indemnitees"), from and against any and all damages, costs, expenses, liabilities, claims, demands, causes of action, proceedings, expenses, judgments, penalties, liens, and losses of any nature whatsoever, including fees of accountants, attorneys, or other professionals and all costs associated therewith and the payment of all consequential damages (collectively "Liabilities"), in law or equity, whether actual, alleged or threatened, which arise out of, are claimed to arise out of, pertain to, or relate to the acts or omissions of Consultant, its officers, agents, servants, employees, subcontractors, materialmen, consultants or their officers, agents, servants or employees (or any entity or individual that Consultant shall bear the legal liability thereof) in the performance of this Agreement, including the Indemnitees' active or passive negligence, except for Liabilities arising from the sole negligence or willful misconduct of the Indemnitees as determined by court decision or by the agreement of the Parties. Consultant shall defend the Indemnitees in any action or actions filed in connection with any Liabilities with counsel of the Indemnitees' choice, and shall pay all costs and expenses, including all attorneys' fees and experts' costs actually incurred in connection with such defense. Consultant shall reimburse the Indemnitees for any and all legal expenses and costs incurred by Indemnitees in connection therewith.

2) Consultant shall pay all required taxes on amounts paid to Consultant under this Agreement, and indemnify and hold City harmless from any and all taxes, assessments, penalties, and interest asserted against City by reason of the independent contractor relationship created by this Agreement. Consultant shall fully comply with the workers' compensation law regarding Consultant and Consultant's employees. Consultant shall indemnify and hold City harmless from any failure of Consultant to comply with applicable workers' compensation laws. City may offset against the amount of any fees due to Consultant under this Agreement any amount due to City from Consultant as a result of Consultant's failure to promptly pay to City any reimbursement or indemnification arising under this subparagraph A.2).

3) Consultant shall obtain executed indemnity agreements with provisions identical to those in this Section from each and every subcontractor or any other person or entity involved by, for, with or on behalf of Consultant in the performance of this Agreement. If Consultant fails to obtain such indemnity obligations, Consultant shall be fully responsible and indemnify, hold harmless and defend the Indemnitees from and against any and all Liabilities at law or in equity, whether actual, alleged or threatened, which arise out of, are claimed to arise out of, pertain to, or relate to the acts or omissions of Consultant's subcontractor, its officers, agents, servants,

employees, subcontractors, materialmen, consultants or their officers, agents, servants or employees (or any entity or individual that Consultant's subcontractor shall bear the legal liability thereof) in the performance of this Agreement, including the Indemnitees' active or passive negligence, except for Liabilities arising from the sole negligence or willful misconduct of the Indemnitees as determined by court decision or by the agreement of the Parties.

B. Workers' Compensation Acts not Limiting. Consultant's indemnifications and obligations under this Section, or any other provision of this Agreement, shall not be limited by the provisions of any workers' compensation act or similar act. Consultant expressly waives its statutory immunity under such statutes or laws as to City, its officers, agents, employees and volunteers.

C. Insurance Requirements not Limiting. City does not, and shall not, waive any rights that it may possess against Consultant because of the acceptance by City, or the deposit with City, of any insurance policy or certificate required pursuant to this Agreement. The indemnities in this Section shall apply regardless of whether or not any insurance policies are determined to be applicable to the Liabilities, tax, assessment, penalty or interest asserted against City.

D. Survival of Terms. Consultant's indemnifications and obligations under this Section shall survive the expiration or termination of this Agreement.

9. Insurance.

A. Minimum Scope and Limits of Insurance. Consultant shall procure and at all times during the term of this Agreement carry, maintain, and keep in full force and effect, insurance as follows:

1) Commercial General Liability Insurance with a minimum limit of \$2,000,000.00 per occurrence for bodily injury, personal injury and property damage and a general aggregate limit of \$2,000,000.00 per project or location. If Consultant is a limited liability company, the commercial general liability coverage shall be amended so that Consultant and its managers, affiliates, employees, agents and other persons necessary or incidental to its operation are insureds.

2) Automobile Liability Insurance for any owned, non-owned or hired vehicle used in connection with the performance of this Agreement with a combined single limit of \$2,000,000.00 per accident for bodily injury and property damage. If Consultant does not use any owned, non-owned or hired vehicles in the performance of Services under this Agreement, Consultant shall obtain a non-owned auto endorsement to the Commercial General Liability policy required under subparagraph A.1) of this Section.

3) Workers' Compensation Insurance as required by the State of California and Employer's Liability Insurance with a minimum limit of \$1,000,000.00 per

accident for bodily injury or disease. If Consultant has no employees while performing Services under this Agreement, workers' compensation policy is not required, but Consultant shall execute a declaration that it has no employees.

4) Professional Liability/Errors and Omissions Insurance with minimum limits of \$2,000,000.00 per claim and in aggregate.

B. Acceptability of Insurers. The insurance policies required under this Section shall be issued by an insurer admitted to write insurance in the State of California with a rating of A:VII or better in the latest edition of the A.M. Best Insurance Rating Guide. Self-insurance shall not be considered to comply with the insurance requirements under this Section.

C. Additional Insured. The commercial general and automobile liability policies shall contain an endorsement naming City and its elected and appointed officials, officers, employees, agents and volunteers as additional insureds. This provision shall also apply to any excess/umbrella liability policies.

D. Primary and Non-Contributing. The insurance policies required under this Section shall apply on a primary non-contributing basis in relation to any other insurance or self-insurance available to City. Any insurance or self-insurance maintained by City, its elected and appointed officials, officers, employees, agents or volunteers, shall be in excess of Consultant's insurance and shall not contribute with it.

E. Consultant's Waiver of Subrogation. The insurance policies required under this Section shall not prohibit Consultant and Consultant's employees, agents or subcontractors from waiving the right of subrogation prior to a loss. Consultant hereby waives all rights of subrogation against City.

F. Deductibles and Self-Insured Retentions. Any deductibles or self-insured retentions must be declared to and approved by City. At City's option, Consultant shall either reduce or eliminate the deductibles or self-insured retentions with respect to City, or Consultant shall procure a bond guaranteeing payment of losses and expenses.

G. Cancellations or Modifications to Coverage. Consultant shall not cancel, reduce or otherwise modify the insurance policies required by this Section during the term of this Agreement. The commercial general and automobile liability policies required under this Agreement shall be endorsed to state that should the issuing insurer cancel the policy before the expiration date, the issuing insurer will endeavor to mail 30 days' prior written notice to City. If any insurance policy required under this Section is canceled or reduced in coverage or limits, Consultant shall, within two Business Days of notice from the insurer, phone, fax or notify City via certified mail, return receipt requested, of the cancellation of or changes to the policy.

H. City Remedy for Noncompliance. If Consultant does not maintain the policies of insurance required under this Section in full force and effect during the term

of this Agreement, or in the event any of Consultant's policies do not comply with the requirements under this Section, City may either immediately terminate this Agreement or, if insurance is available at a reasonable cost, City may, but has no duty to, take out the necessary insurance and pay, at Consultant's expense, the premium thereon. Consultant shall promptly reimburse City for any premium paid by City or City may withhold amounts sufficient to pay the premiums from payments due to Consultant.

I. Evidence of Insurance. Prior to the performance of Services under this Agreement, Consultant shall furnish City's Risk Manager with a certificate or certificates of insurance and all original endorsements evidencing and effecting the coverages required under this Section. The endorsements are subject to City's approval. Consultant may provide complete, certified copies of all required insurance policies to City. Consultant shall maintain current endorsements on file with City's Risk Manager. Consultant shall provide proof to City's Risk Manager that insurance policies expiring during the term of this Agreement have been renewed or replaced with other policies providing at least the same coverage. Consultant shall furnish such proof at least two weeks prior to the expiration of the coverages.

J. Indemnity Requirements not Limiting. Procurement of insurance by Consultant shall not be construed as a limitation of Consultant's liability or as full performance of Consultant's duty to indemnify City under Section 8 of this Agreement.

K. Broader Coverage/Higher Limits. If Consultant maintains broader coverage and/or higher limits than the minimums required above, City requires and shall be entitled to the broader coverage and/or the higher limits maintained by Consultant. Any available insurance proceeds in excess of the specified minimum limits of insurance and coverage shall be available to City.

L. Subcontractor Insurance Requirements. Consultant shall require each of its subcontractors that perform Services under this Agreement to maintain insurance coverage that meets all of the requirements of this Section.

10. Mutual Cooperation.

A. City's Cooperation. City shall provide Consultant with all pertinent Data, documents and other requested information as is reasonably available for Consultant's proper performance of the Services required under this Agreement.

B. Consultant's Cooperation. In the event any claim or action is brought against City relating to Consultant's performance of Services rendered under this Agreement, Consultant shall render any reasonable assistance that City requires.

11. Records and Inspections. Consultant shall maintain complete and accurate records with respect to time, costs, expenses, receipts, correspondence, and other such information required by City that relate to the performance of the Services. All such

records shall be maintained in accordance with generally accepted accounting principles and shall be clearly identified and readily accessible. Consultant shall provide free access to City, its designees and representatives at reasonable times, and shall allow City to examine and audit the books and records, to make transcripts therefrom as necessary, and to inspect all work, data, documents, proceedings and activities related to this Agreement. Such records, together with supporting documents, shall be maintained for a period of three years after receipt of final payment.

12. Termination of Agreement.

A. Right to Terminate. City may terminate this Agreement at any time, at will, for any reason or no reason, after giving written notice to Consultant at least five calendar days before the termination is to be effective. Consultant may terminate this Agreement at any time, at will, for any reason or no reason, after giving written notice to City at least 60 calendar days before the termination is to be effective.

B. Obligations upon Termination. Consultant shall cease all work under this Agreement on or before the effective date of termination specified in the notice of termination. In the event of City's termination of this Agreement due to no fault or failure of performance by Consultant, City shall pay Consultant based on the percentage of work satisfactorily performed up to the effective date of termination. In no event shall Consultant be entitled to receive more than the amount that would be paid to Consultant for the full performance of the Services required by this Agreement. Consultant shall have no other claim against City by reason of such termination, including any claim for compensation.

13. Force Majeure. Consultant shall not be liable for any failure to perform its obligations under this Agreement if Consultant presents acceptable evidence, in City's sole judgment, that such failure was due to acts of God, embargoes, inability to obtain labor or materials or reasonable substitutes for labor or materials, governmental restrictions, governmental regulations, governmental controls, judicial orders, enemy or hostile governmental action, civil commotion, fire or other casualty, or other causes beyond Consultant's reasonable control and not due to any act by Consultant.

14. Default.

A. Consultant's failure to comply with the provisions of this Agreement shall constitute a default. In the event that Consultant is in default for cause under the terms of this Agreement, City shall have no obligation or duty to continue compensating Consultant for any work performed after the date of default.

B. In addition to the right to terminate pursuant to Section 12, if the City Manager determines that Consultant is in default in the performance of any of the terms or conditions of this Agreement, City shall serve Consultant with written notice of the default. Consultant shall have ten calendar days after service upon it of the notice in which to cure the default by rendering a satisfactory performance. In the event that

Consultant fails to cure its default within such period of time, City may, notwithstanding any other provision of this Agreement, terminate this Agreement without further notice and without prejudice to any other remedy to which it may be entitled at law, in equity or under this Agreement.

15. Notices. Any notice, consent, request, demand, bill, invoice, report or other communication required or permitted under this Agreement shall be in writing and conclusively deemed effective: (a) on personal delivery, (b) on confirmed delivery by courier service during Consultant's and City's regular business hours, or (c) three Business Days after deposit in the United States mail, by first class mail, postage prepaid, and addressed to the Party to be notified as set forth below:

TO CITY:

City of Manhattan Beach
Attn: Engineering, Anastasia Seims
1400 Highland Avenue
Manhattan Beach, California 90266

TO CONSULTANT:

Arudrra Group, Inc.
Attn: Dino D'Emilia
1960 E. Grand Avenue, Suite 300
El Segundo, California 90245

COPY TO CITY ATTORNEY:

City of Manhattan Beach
Attn: City Attorney
1400 Highland Avenue
Manhattan Beach, CA 90266

16. Non-Discrimination and Equal Employment Opportunity. In the performance of this Agreement, Consultant shall not discriminate against any employee, subcontractor or applicant for employment because of race, color, religious creed, sex, gender, gender identity, gender expression, marital status, national origin, ancestry, age, physical disability, mental disability, medical condition, genetic information, sexual orientation or other basis prohibited by law. Consultant will take affirmative action to ensure that subcontractors and applicants are employed, and that employees are treated during employment, without regard to their race, color, religious creed, sex, gender, gender identity, gender expression, marital status, national origin, ancestry, age, physical disability, mental disability, medical condition, genetic information or sexual orientation.

17. Prohibition of Assignment and Delegation. Consultant shall not assign any of its rights or delegate any of its duties under this Agreement, either in whole or in part, without City's prior written consent. City's consent to an assignment of rights under this Agreement shall not release Consultant from any of its obligations or alter any of its primary obligations to be performed under this Agreement. Any attempted assignment or delegation in violation of this Section shall be void and of no effect and shall entitle City to terminate this Agreement. As used in this Section, "assignment" and

“delegation” means any sale, gift, pledge, hypothecation, encumbrance or other transfer of all or any portion of the rights, obligations, or liabilities in or arising from this Agreement to any person or entity, whether by operation of law or otherwise, and regardless of the legal form of the transaction in which the attempted transfer occurs.

18. No Third Party Beneficiaries Intended. This Agreement is made solely for the benefit of the Parties to this Agreement and their respective successors and assigns, and no other person or entity may have or acquire a right by virtue of this Agreement.

19. Waiver. No delay or omission to exercise any right, power or remedy accruing to City under this Agreement shall impair any right, power or remedy of City, nor shall it be construed as a waiver of, or consent to, any breach or default. No waiver of any breach, any failure of a condition, or any right or remedy under this Agreement shall be (1) effective unless it is in writing and signed by the Party making the waiver, (2) deemed to be a waiver of, or consent to, any other breach, failure of a condition, or right or remedy, or (3) deemed to constitute a continuing waiver unless the writing expressly so states.

20. Final Payment Acceptance Constitutes Release. The acceptance by Consultant of the final payment made under this Agreement shall operate as and be a release of City from all claims and liabilities for compensation to Consultant for anything done, furnished or relating to Consultant’s work or services. Acceptance of payment shall be any negotiation of City’s check or the failure to make a written extra compensation claim within ten calendar days of the receipt of that check. However, approval or payment by City shall not constitute, nor be deemed, a release of the responsibility and liability of Consultant, its employees, subcontractors and agents for the accuracy and competency of the information provided and/or work performed; nor shall such approval or payment be deemed to be an assumption of such responsibility or liability by City for any defect or error in the work prepared by Consultant, its employees, subcontractors and agents.

21. Corrections. In addition to the above indemnification obligations, Consultant shall correct, at its expense, all errors in the work which may be disclosed during City’s review of Consultant’s report or plans. Should Consultant fail to make such correction in a reasonably timely manner, such correction may be made by City, and the cost thereof shall be charged to Consultant. In addition to all other available remedies, City may deduct the cost of such correction from any retention amount held by City or may withhold payment otherwise owed Consultant under this Agreement up to the amount of the cost of correction.

22. Non-Appropriation of Funds. Payments to be made to Consultant by City for services performed within the current fiscal year are within the current fiscal budget and within an available, unexhausted fund. In the event that City does not appropriate sufficient funds for payment of Consultant’s services beyond the current fiscal year, this Agreement shall cover payment for Consultant’s services only to the conclusion of the

last fiscal year in which City appropriates sufficient funds and shall automatically terminate at the conclusion of such fiscal year.

23. Exhibits. Exhibits A, B and C constitute a part of this Agreement and are incorporated into this Agreement by this reference. If any inconsistency exists or arises between a provision of this Agreement and a provision of any exhibit, or between a provision of this Agreement and a provision of Consultant's proposal, the provisions of this Agreement shall control.

24. Entire Agreement and Modification of Agreement. This Agreement and all exhibits referred to in this Agreement constitute the final, complete and exclusive statement of the terms of the agreement between the Parties pertaining to the subject matter of this Agreement and supersede all other prior or contemporaneous oral or written understandings and agreements of the Parties. No Party has been induced to enter into this Agreement by, nor is any Party relying on, any representation or warranty except those expressly set forth in this Agreement. This Agreement may not be amended, nor any provision or breach hereof waived, except in a writing signed by both Parties.

25. Headings. The headings in this Agreement are included solely for convenience of reference and shall not affect the interpretation of any provision of this Agreement or any of the rights or obligations of the Parties to this Agreement.

26. Word Usage. Unless the context clearly requires otherwise, (a) the words "shall," "will" and "agrees" are mandatory and "may" is permissive; (b) "or" is not exclusive; and (c) "includes" or "including" are not limiting.

27. Time of the Essence. Time is of the essence in respect to all provisions of this Agreement that specify a time for performance; provided, however, that the foregoing shall not be construed to limit or deprive a Party of the benefits of any grace or use period allowed in this Agreement.

28. Business Days. "Business days" means days Manhattan Beach City Hall is open for business.

29. Governing Law and Choice of Forum. This Agreement, and any dispute arising from the relationship between the Parties to this Agreement, shall be governed by and construed in accordance with the laws of the State of California, except that any rule of construction to the effect that ambiguities are to be resolved against the drafting party shall not be applied in interpreting this Agreement. Any dispute that arises under or relates to this Agreement (whether contract, tort or both) shall be resolved in a superior court with geographic jurisdiction over the City of Manhattan Beach.

30. Attorneys' Fees. In any litigation or other proceeding by which a Party seeks to enforce its rights under this Agreement (whether in contract, tort or both) or seeks a declaration of any rights or obligations under this Agreement, the prevailing Party shall

be entitled to recover all attorneys' fees, experts' fees, and other costs actually incurred in connection with such litigation or other proceeding, in addition to all other relief to which that Party may be entitled.

31. Severability. If a court of competent jurisdiction holds any provision of this Agreement to be illegal, invalid or unenforceable for any reason, the validity of and enforceability of the remaining provisions of this Agreement shall not be affected and continue in full force and effect.

32. Counterparts. This Agreement may be executed in multiple counterparts, all of which shall be deemed an original, and all of which will constitute one and the same instrument.

33. Corporate Authority. Each person executing this Agreement on behalf of his or her Party warrants that he or she is duly authorized to execute this Agreement on behalf of that Party and that by such execution, that Party is formally bound to the provisions of this Agreement.

[SIGNATURE PAGE FOLLOWS]

The Parties, through their duly authorized representatives are signing this Agreement on the date stated in the introductory clause.

City:

City of Manhattan Beach,
a California municipal corporation

Consultant:

Ardurra Group, Inc.,
a Florida corporation

DocuSigned by:
By: Bruce Moe 10/25/2021
EAD3C08846884FC...
Name: Bruce Moe
Title: City Manager

DocuSigned by:
By: Lisa Penna 9/20/2021
CA9610FB9C8D4B3...
Name: Lisa Penna
Title: Managing Principal

ATTEST:

DocuSigned by:
By: Dino D'Emilia 9/20/2021
755F7606CBA54C3...
Name: Dino D'Emilia
Title: PMCM Group Leader

DocuSigned by:
By: Liza Tamura 11/3/2021
0826026E3681486...
Name: Liza Tamura
Title: City Clerk

**PROOF OF AUTHORITY TO BIND
CONTRACTING PARTY REQUIRED**

APPROVED AS TO FORM:

DocuSigned by:
By: Quinn Barrow 9/23/2021
96FA866DA074E9...
Name: Quinn M. Barrow
Title: City Attorney

APPROVED AS TO FISCAL IMPACT:


DocuSigned by:
By: Steve Charelian 9/23/2021
1A2E390F2B9C494...
Name: Steve S. Charelian
Title: Finance Director

APPROVED AS TO CONTENT:

DocuSigned by:
By: Erick Lee 9/23/2021
F9F4AFF3A992452...
Name: Erick Lee
Title: Public Works Director

EXHIBIT A SCOPE OF SERVICES

PROJECT TEAM ORGANIZATION CHART

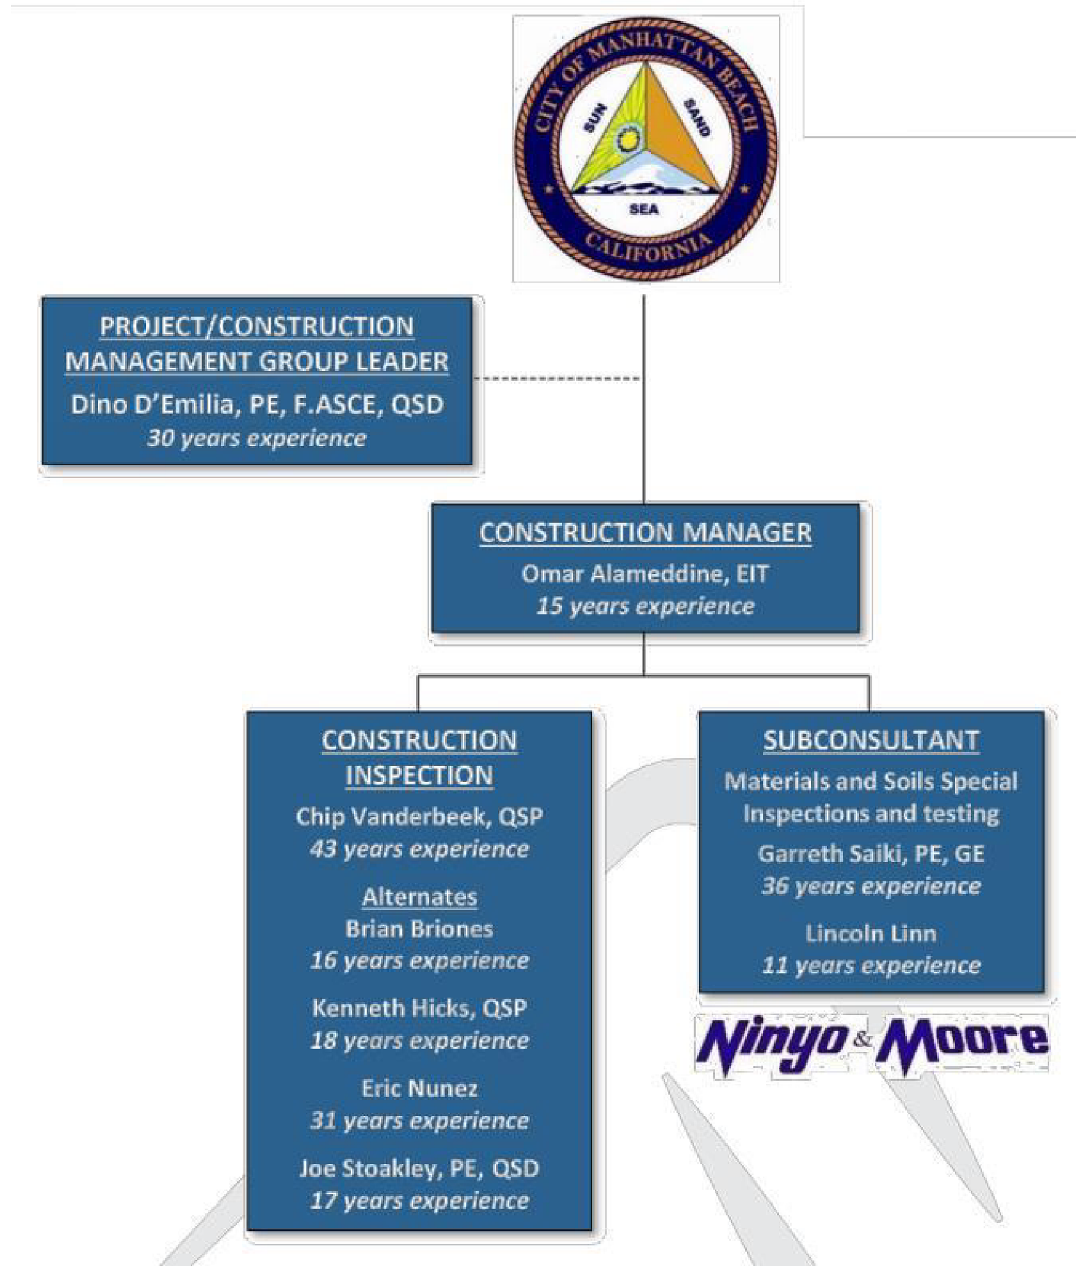

SCOPE OF SERVICES

Ardurra will provide full-time oversight of the Contractor through the performance of project inspection services, special inspection services, and construction management. Ardurra's services will be provided from start to completion of the Polliwog Park Lower Playground Replacement Project (Project) to oversee, monitor, and document that the Contractor performs all the necessary work as described in the contract documents for Project No. M-985, Bid No. E1262-21C, as well as other tasks identified herein. All work will be performed to the industry professional standards and will reflect the thoroughness, attention to detail and professional knowledge expected in overview of all the associated construction phases.

Ardurra's project inspector and construction manager will be required during preconstruction, construction, and closeout for the Project. Construction is expected to start by early November 2021, and the construction contract includes 110 working days. Ardurra's project inspector will be on-site for the entire duration of the construction, and as-needed for closeout of the Project. Ardurra will be responsible for construction management and inspection, which includes but is not limited to the overall contract compliance, contract change order review, schedule changes, construction inspections, and quantity calculations and verifications. Examples of specific tasks included in the scope of services are listed below. Ardurra will collaborate and work cooperatively with the City's project manager assigned to the project.

The typical workday includes all hours worked by the construction Contractor. The construction Contractor's operations may be restricted to specific hours during the week, which shall become the normal workday for Consultant personnel. The Consultant Project Manager, with concurrence from the City, shall have the authority to increase, decrease, or eliminate Consultant personnel work hours dependent on the schedule and requirements of the construction Contractor.

Project Inspection Tasks

- A. Reviewing the contract documents, including plans, specifications, and quantities prior to the preconstruction meeting;
- B. Attend the Preconstruction Meeting;
- C. Documenting, with digital images and video, the preconstruction existing conditions of the work areas and project areas;
- D. Establishing effective communication with the Contractor, City staff, property owners, Manhattan Beach Unified School District and the general public;
- E. Providing full-time inspection services to ensure compliance with the Contract Documents and other requirements, such as, but not limited to, Work Area Traffic Control Handbook (WATCH Manual) or Manual on Uniform Traffic Control

Devices (MUTCD) California (Latest Edition), Cal/OSHA Standards, contract change orders, permits, California Building Code and ASTM standards;

- F. Evaluating the Contractor's daily performance and addressing deficiencies as they occur;
- G. Coordinating any field issues that require deviations from the Contract Documents with the City's Project Manager (noting that the Consultant project inspector does not have the authority to allow deviations from the Contract Documents and shall receive authorization for any deviation from the City's Project Manager);
- H. Provide day-to-day on-the-job observation/inspection of all construction work on the project. Consultant inspectors shall make reasonable efforts to guard the City against defects and deficiencies in the work of the Contractor and to ensure provisions of the contract documents are being fulfilled; prepare daily inspection reports documenting observed construction activities; document the names, classifications, tasks completed, and hours worked of all contractor crew members completing work onsite; take progress photographs (digital) of all work and project locations and log and label in specific logical electronic folders; and assist with all other matters relating to construction of the project. Daily Inspection Reports shall be submitted to the City's Project Manager on the next business day for review and filing. Consultant to provide example of form to be used to City for review and approval prior to start of construction;
- I. Submitting to the City on a weekly basis a Weekly Statement of Working Days for the project;
- J. Attending regularly-scheduled construction meetings;
- K. Verify layout of work prior to the beginning of the permanent work;
- L. Measure and tabulate contract quantities, review the Contractor's invoices, verify completed work, approve all quantities, and assist with meetings with the Contractor to resolve any differences in percent complete;
- M. Obtaining and reviewing the Contractor's daily reports;
- N. Logging, tracking and responding to all concerns and complaints from the public in an expeditious manner;
- O. Reviewing material test reports to substantiate contract compliance;
- P. Coordinating and monitoring Contractor's operations with subcontractor trades, suppliers, special inspectors/lab testing technicians, utility companies, Manhattan

Beach Unified School District, neighboring residents and other affected parties as needed;

- Q. Coordinating/ensuring utilities are shut off and abatement needs are identified prior to demolition;
- R. Monitor extra work, and provide supporting documentation on the personnel and equipment that is involved with any extra work performed by the Contractor. Determine whether the work of the Contractor is being performed in accordance with the requirements of the contract documents, and endeavor to guard the City against defects and deficiencies in such work. Extra work personnel and equipment shall be documented separately of contract work and included in the Daily Inspection Reports submitted to the City. It shall be clear in this documentation which equipment and personnel (name and title) worked on extra work or disputed work versus contract work and for what durations;
- S. Monitoring and enforcing Contractor's compliance with BMPs;
- T. Monitoring safety and health requirements and enforcing applicable regulations and contract provisions for the protection of the public and project personnel;
- U. Performing project oversight for the monitoring of damage to existing infrastructure and replacement of infrastructure to City standards;
- V. Documenting all Contractor delays, reasons for delay, length of time for delay, and phases of work;
- W. Documenting changes in the field to compare to the Contractor's record drawings;
- X. Recommending courses of action when the Contractor's or subcontractor's performance is unsatisfactory and assist in carrying out the necessary corrective actions;
- Y. Completing incident (accident) reports;
- Z. Confirm on a monthly basis that the Contractor is maintaining up-to-date marked up prints of construction drawings and documents showing all field changes and as-built conditions;
- AA. At the completion of the work, review the Contractor's redline as-builts to ensure all field changes and as-built conditions are identified;
- BB. Incorporating approved changes to the plans, specifications, and contract documents as they occur and ensure that the red-line set for the as-built is maintained on a regular basis;

- CC. Preparing status reports for project close-out and all collecting documents as a closeout file;
- DD. Conducting project walk-through(s) and preparing a list of items for correction (punch list);
- EE. Performing a final project inspection;
- FF. Performing warranty walks, approximately one (1) year from the City Council acceptance of the project;
- GG. Performing and/or assisting with all other related duties as required;
- HH. Possessing a vehicle with auto insurance and valid California driver's license, and a mobile phone for immediate contact by the City; and
- II. Performing inspections during Normal Contractor Work Hours, Monday through Friday, 7:30 a.m. to 4:30p.m., excluding holidays.

Special Inspection Tasks

- A. Providing special inspections for soils, play structure foundations, and others as needed and as identified in the Project Documents. This scope is to be performed by Ardurra Group, Inc.'s subconsultant, Ninyo & Moore.

Construction Management Tasks

- A. Reviewing the contract documents, including plans, specifications, and quantities prior to the preconstruction meeting;
- B. Attend the Preconstruction Meeting;
- C. Providing administrative, management, and related services necessary to coordinate the work of the General Contractor and all subcontractors in order to facilitate timely completion of the project in accordance with the City objectives.
- D. Assisting the Contractor and City with public notifications, public relations, and public outreach regarding the Project;
- E. Review work progress as compared to the Project Baseline Schedule and inform the City Project Manager of schedule slippage;
- F. Monitoring and reporting on the status of project and project construction budget on a monthly basis, indicating the actual costs for completed activities and work in progress, and indicating estimates for uncompleted work;

- G. Identifying variances between actual and budgeted or estimated costs, and advising the City whenever it appears that the construction budget has or will be exceeded for the project as a whole or any project component;
- H. Maintaining cost accounting records on actual work performed under unit costs or a Schedule of Values (in the event that force account procedures are used or other work monitoring requires accounting records);
- I. Recommending courses of action when the Contractor's or subcontractor's performance is unsatisfactory and assist in carrying out the necessary corrective actions;
- J. Maintaining contiguous 24-hour telephone accessibility of the construction activity for emergency use;
- K. Assisting the Contractor in obtaining all building, grading, and other permits necessary for the project;
- L. Ensuring that the following prevailing wage requirements are met:
 - a. Contractor posts a list of prevailing wages in the area for the work to be performed on the project, as required pursuant to Labor Code 1770, in a prominent place at the project site;
 - b. Reviewing all certified payrolls for conformance to the prevailing wage rates;
- M. Providing, managing, coordinating, and ensuring timely completion/approvals in response to all RFIs, shop drawings, product data samples, Change Notices, Intent to File Change notice, and Construction Change Orders (CCOs) review, negotiations and issuance of Change order to the Contractor;
- N. Following the established City procedures in processing Contract Change Orders (CCO), which are:
 - a. Reviewing requests for change orders received from the Contractor;
 - b. Recommending necessary or desirable project changes to the City;
 - c. Assisting the City in CCO negotiations;
 - d. Submitting recommendations to the City relative to change order requests; and
 - e. Preparing the CCO(s) and obtaining the Contractor's signature.

- O. Preparing independent cost estimates for comparison and review by the City for all Contractor-submitted change notices/orders;
- P. Coordinating shop drawings and RFI review and approval;
- Q. Reviewing Contractor pay requests and preparing the necessary documentation for submittal and approval by the City.
- R. Tracking all invoices and progress payments in accordance with City policies and Procedures;
- S. Maintaining the project site record copies of the following:
 - a. Plans, specifications, and contract documents with all changes and modifications;
 - b. Permits;
 - c. Addenda, Change order(s), shop drawings, product data, submittals and samples;
 - d. Progress payments, inventories, and applicable codes;
 - e. Contractor's reports, correspondence, certified payroll records, and accident reports;
 - f. Survey and layout data and certifications, photographs of as-built locations and depths; and
 - g. List of addresses, telephone and license numbers of General Contractor, all subcontractors, material suppliers, and utility agencies.
- T. Coordinating close-out of the project, obtaining the necessary operation manuals, warranty, guarantees, and other applicable necessary information and providing all documentation in a well-organized manner in electronic and hard copy formats (binders, folders, flash drives, etc.);
- U. Obtaining releases and warranty bonds from the General Contractor and sub-contractors, and providing all documentation in a well-organized manner in electronic and hard copy formats (binders, folders, flash drives, etc.);
- V. Delivering all keys, manuals, and record drawings to the City and coordinate all final inspections, and provide all documentation in a well-organized manner in electronic and hard copy formats (binders, folders, flash drives, etc.);
- W. Preparing status reports for project close-out;

- X. Presenting City with a complete project close-out file;
- Y. Performing such other project-related duties as may be required by the City; and
- Z. Resolving all warranty issues so that the City can release the Warranty Bond.

**EXHIBIT B
APPROVED FEE SCHEDULE**

Pre-Construction		5 Days		
TITLE	Est. Hours Per Day	Total Hours	Hourly Rate 1,	Extended Fee
Principal-In-Charge / QA/QC	0.00	0.00	\$ 230.00	\$ -
Construction Manager	1.50	7.50	\$ 200.00	\$ 1,500.00
Construction Inspector ^{3, 4, 5}	1.00	5.00	\$ 145.00	\$ 725.00
Project Controls Engineer	2.00	10.00	\$ 135.00	\$ 1,350.00
Subtotal Pre-Construction				\$ 3,575.00
Construction		140 Days		
TITLE	Est. Hours Per Day	Total Hours	Hourly Rate 1,	Extended Fee
Principal-In-Charge / QA/QC	0.00	0.00	\$ 230.00	\$ -
Construction Manager Oversight	1.00	140.00	\$ 200.00	\$ 28,000.00
Construction Inspector ^{3, 4, 5}	8.00	1,120.00	\$ 145.00	\$ 162,400.00
Project Controls Engineer	3.00	420.00	\$ 135.00	\$ 56,700.00
Subtotal Construction				\$ 247,100.00
Post-Construction		5 Days		
TITLE	Est. Hours Per Day	Total Hours	Hourly Rate 1,	Extended Fee
Principal-In-Charge / QA/QC	0.00	0.00	\$ 230.00	\$ -
Construction Manager Oversight	1.50	7.50	\$ 200.00	\$ 1,500.00
Construction Inspector ^{3, 4, 5}	4.00	20.00	\$ 145.00	\$ 2,900.00
Project Controls Engineer	3.00	15.00	\$ 135.00	\$ 2,025.00
Subtotal Post-Construction				\$ 6,425.00
Other Direct Costs				
Item				Amount
Procure License Fee (Based on \$2M Estimated Construction Value)				\$ 4,000.00
Miscellaneous ODCs (Allowance)				\$ 8,000.00
Subtotal Other Direct Costs				\$ 12,000.00
SUBTOTAL CM SERVICES				\$ 269,100.00
Optional Services				
Item				Extended Fee
Geotechnical Services (Allowance - Detailed fee will be provided / adjusted upon receipt of construction CPM Schedule)				\$ 25,000.00
Subtotal Optional Services				\$ 25,000.00
Total Estimated Fee with Optional Services				\$ 294,100.00

EXHIBIT C

TERMS FOR COMPLIANCE WITH CALIFORNIA LABOR LAW REQUIREMENTS

1. This Agreement calls for services that, in whole or in part, constitute “public works” as defined in Division 2, Part 7, Chapter 1 (commencing with Section 1720) of the California Labor Code (“Chapter 1”). Further, Contractor acknowledges that this Agreement is subject to (a) Chapter 1 and (b) the rules and regulations established by the Department of Industrial Relations (“DIR”) implementing such statutes. Therefore, as to those Services that are “public works”, Contractor shall comply with and be bound by all the terms, rules and regulations described in 1(a) and 1(b) as though set forth in full herein.

2. California law requires the inclusion of specific Labor Code provisions in certain contracts. The inclusion of such specific provisions below, whether or not required by California law, does not alter the meaning or scope of Section 1 above.

3. Contractor shall be registered with the Department of Industrial Relations in accordance with California Labor Code Section 1725.5, and has provided proof of registration to City prior to the Effective Date of this Agreement. Contractor shall not perform work with any subcontractor that is not registered with DIR pursuant to Section 1725.5. Contractor and subcontractors shall maintain their registration with the DIR in effect throughout the duration of this Agreement. If the Contractor or any subcontractor ceases to be registered with DIR at any time during the duration of the project, Contractor shall immediately notify City.

4. Pursuant to Labor Code Section 1771.4, Contractor’s Services are subject to compliance monitoring and enforcement by DIR. Contractor shall post job site notices, as prescribed by DIR regulations.

5. Pursuant to Labor Code Section 1773.2, copies of the prevailing rate of per diem wages for each craft, classification, or type of worker needed to perform the Agreement are on file at City Hall and will be made available to any interested party on request. Contractor acknowledges receipt of a copy of the DIR determination of such prevailing rate of per diem wages, and Contractor shall post such rates at each job site covered by this Agreement.

6. Contractor shall comply with and be bound by the provisions of Labor Code Sections 1774 and 1775 concerning the payment of prevailing rates of wages to workers and the penalties for failure to pay prevailing wages. The Contractor shall, as a penalty to City, forfeit \$200.00 for each calendar day, or portion thereof, for each worker paid less than the prevailing rates as determined by the DIR for the work or craft in which the worker is employed for any public work done pursuant to this Agreement by Contractor or by any subcontractor.

7. Contractor shall comply with and be bound by the provisions of Labor Code Section 1776, which requires Contractor and each subcontractor to: keep accurate payroll records and verify such records in writing under penalty of perjury, as specified in Section 1776; certify and make such payroll records available for inspection as provided by Section 1776; and inform City of the location of the records. Pursuant to Labor Code Section 1771.4, Contractor and each subcontractor shall furnish such records to the Labor Commissioner, at least monthly, in the form specified by the Labor Commissioner.

8. Contractor shall comply with and be bound by the provisions of Labor Code Sections 1777.5, 1777.6 and 1777.7 and California Administrative Code Title 8, Section 200 et seq. concerning the employment of apprentices on public works projects. Contractor shall be responsible for compliance with these aforementioned Sections for all apprenticeable occupations. Prior to commencing work under this Agreement, Contractor shall provide City with a copy of the information submitted to any applicable apprenticeship program. Within 60 days after concluding work pursuant to this Agreement, Contractor and each of its subcontractors shall submit to City a verified statement of the journeyman and apprentice hours performed under this Agreement.

9. The Contractor shall not perform Work with any Subcontractor that has been debarred or suspended pursuant to California Labor Code Section 1777.1 or any other federal or state law providing for the debarment of contractors from public works. The Contractor and Subcontractors shall not be debarred or suspended throughout the duration of this Contract pursuant to Labor Code Section 1777.1 or any other federal or state law providing for the debarment of contractors from public works. If the Contractor or any subcontractor becomes debarred or suspended during the duration of the project, the Contractor shall immediately notify City.

10. Contractor acknowledges that eight hours labor constitutes a legal day's work. Contractor shall comply with and be bound by Labor Code Section 1810. Contractor shall comply with and be bound by the provisions of Labor Code Section 1813 concerning penalties for workers who work excess hours. The Contractor shall, as a penalty to City, forfeit \$25.00 for each worker employed in the performance of this Agreement by the Contractor or by any subcontractor for each calendar day during which such worker is required or permitted to work more than eight hours in any one calendar day and 40 hours in any one calendar week in violation of the provisions of Division 2, Part 7, Chapter 1, Article 3 of the Labor Code. Pursuant to Labor Code section 1815, work performed by employees of Contractor in excess of eight hours per day, and 40 hours during any one week shall be permitted upon public work upon compensation for all hours worked in excess of eight hours per day at not less than one and one-half times the basic rate of pay.

11. California Labor Code Sections 1860 and 3700 provide that every employer will be required to secure the payment of compensation to its employees. In accordance with the provisions of California Labor Code Section 1861, Contractor hereby certifies as follows:

“I am aware of the provisions of Section 3700 of the Labor Code which require every employer to be insured against liability for workers’ compensation or to undertake self-insurance in accordance with the provisions of that code, and I will comply with such provisions before commencing the performance of the work of this contract.”

12. For every subcontractor who will perform work on the project, Contractor shall be responsible for such subcontractor’s compliance with Chapter 1 and Labor Code Sections 1860 and 3700, and Contractor shall include in the written contract between it and each subcontractor a copy of those statutory provisions and a requirement that each subcontractor shall comply with those statutory provisions. Contractor shall be required to take all actions necessary to enforce such contractual provisions and ensure subcontractor’s compliance, including without limitation, conducting a periodic review of the certified payroll records of the subcontractor and upon becoming aware of the failure of the subcontractor to pay his or her workers the specified prevailing rate of wages. Contractor shall diligently take corrective action to halt or rectify any failure.

13. To the maximum extent permitted by law, Contractor shall indemnify, hold harmless and defend (at Contractor’s expense with counsel reasonably acceptable to City) City, its officials, officers, employees, agents and independent contractors serving in the role of City officials, and volunteers from and against any demand or claim for damages, compensation, fines, penalties or other amounts arising out of or incidental to any acts or omissions listed above by any person or entity (including Contractor, its subcontractors, and each of their officials, officers, employees and agents) in connection with any work undertaken or in connection with the Agreement, including without limitation the payment of all consequential damages, attorneys’ fees, and other related costs and expenses. All duties of Contractor under this Section shall survive the termination of the Agreement.

AMENDMENT NO. 1 TO THE PROFESSIONAL SERVICES AGREEMENT
BETWEEN THE CITY OF MANHATTAN BEACH AND ARDURRA GROUP INC.

This First Amendment (“Amendment No. 1”) to that certain agreement by and between the City of Manhattan Beach, a California municipal corporation (“City”) and Ardurra Group, Inc., a Florida corporation (“Consultant”) (collectively, the “Parties”) is hereby made effective as of the date of the last authorized representative signature below (“Effective Date”).

RECITALS

A. On October 19, 2021, the City and Consultant entered into an agreement for professional services for the Consultant to provide inspection and construction management services for the Polliwog Park Lower Playground Replacement Project (“Agreement”).

B. The Parties now desire to amend the Agreement to increase the Maximum Compensation and modify the Scope of Services and Approved Fee Schedule.

NOW, THEREFORE, in consideration of the Parties’ performance of the promises, covenants, and conditions stated herein, the Parties hereby agree as follows:

Section 1. Section 3. A of the Agreement is hereby revised to increase the Maximum Compensation amount by \$152,598.18, for a new Maximum Compensation of \$446,698.18.

Section 2. Exhibit A (Scope of Services) of the Agreement is hereby amended to add the attached Exhibit A of this Amendment No. 1.

Section 3. Exhibit B (Approved Fee Schedule) of the Agreement is hereby amended to add the attached Exhibit B of this Amendment No. 1.

Section 4. Except as specifically amended by this Amendment No. 1, all other provisions of the Agreement shall remain in full force and effect.

[SIGNATURE PAGE FOLLOWS]

IN WITNESS THEREOF, the Parties hereto have executed this Amendment No. 1 on the day and year first shown above.

City:

Consultant:

City of Manhattan Beach,
a California municipal corporation

Ardurra Group Inc.,
a Florida Corporation

DocuSigned by:
Bruce Moe
By: _____
Name: Bruce Moe 12/21/2022
Title: City Manager

DocuSigned by:
Lisa M. Penna, Vice President Regional Director
By: _____
Name: Lisa Penna, PE 12/5/2022
Title: Vice President, Regional Director

ATTEST:

DocuSigned by:
Liza Tamura
By: _____
Name: Liza Tamura 12/21/2022
Title: City Clerk

DocuSigned by:
Cathy Cahill, CFO
By: _____
Name: Cathy Cahill 12/6/2022
Title: Chief Financial Officer

APPROVED AS TO FORM:

DocuSigned by:
Quinn Barrow, City Attorney
By: _____
Name: Quinn M. Barrow 12/6/2022
Title: City Attorney

APPROVED AS TO FISCAL IMPACT:

DocuSigned by:
Steve S Charelian, Finance Director
By: _____
Name: Steve S. Charelian 12/6/2022
Title: Finance Director

APPROVED AS TO CONTENT:

DocuSigned by:
Erick Lee
By: _____
Name: Erick Lee 12/6/2022
Title: Public Works Director

EXHIBIT A SCOPE OF SERVICES

September 26, 2022

Katherine Doherty, PE, ENV SP, City Engineer
City of Manhattan Beach
3621 Bell Avenue
Manhattan Beach, CA, 90266

Subject: Amendment Request for Extended Professional Construction Management (CM) and Inspection Services for the Manhattan Beach Polliwog Park Lower Playground Replacement Project

Dear Ms. Doherty,

Ardurra Group, Inc. (Ardurra) respectfully requests a contract amendment from the City of Manhattan Beach (City) for the subject project's extended schedule and services outside the scope of our original contract for construction management (CM), inspection, and related services.

Project Understanding

Ardurra's original contract was to provide required services for a period of 140 construction days along with 10 additional days for preconstruction and post-construction activities, beginning on the Ardurra contract execution date of October 19, 2021, and ending tentatively in March 2022. As previously discussed and documented with City representatives in an email sent on February 17, 2022, and in the original amendment request submitted on May 10, 2022, the previously-documented issues continue to have substantial impacts on the project. The completion date and the level of effort required to complete the project has resulted in additional costs for construction management services.

Ardurra's involvement prior to issuance of the Notice of Proceed (NTP) and during the contractor's demobilization period resulted in an increased effort to move the project forward through a projected completed date of February 6, 2023, and the additional tasks listed below.

- Issuance of the Notice to Proceed and delay of the construction start date:
 - Discuss with the City Engineer the negative impacts of issuing an NTP with the selected procurement method, Owner Furnished Contractor Installed (OFCI), without the confirmation of the play equipment delivery.
 - Facilitate the issuance of an administrative NTP to begin the submittal review process and assisted the Contractor with submittal identification, reiterating the necessity to submit the required documents.
 - Assist the Contractor in preparing the Critical Path Method (CPM) schedule through various drafts due to the unusual circumstances surrounding unknown delivery timelines.
 - Coordinate mobilization date with the contractor to mitigate additional delays to the completion of the project.

- Coordination efforts related to the shade sail deferred submittal:
 - Coordinate review meetings to ensure shade sail heights align with the play equipment clearances and achieve the City's vision for the park.
 - Track and follow up with the Contractor and shade sail vendor through design, engineering, and procurement.
- Requested coordination efforts to accommodate the City's request to assess the repurposing of the old Polliwog Park swing set to El Porto Park.
- Additional coordination efforts with the equipment vendor, Kompan, for the delayed delivery of the park equipment and receiving and offloading of the shipment by the Contractor:
 - Tracking of Playground Equipment Shipment:
 - Continual coordination and communication between the City, Kompan, and Ardurra regarding:
- Procurement and production delays due to manufacturing in the Czech Republic.
- Shipment and port entry delays.
- Facilitating play equipment delivery – shipment #1:
- Continual coordination and communication between the City, Kompan, and Ardurra included, but not limited to the following:
 - Identification of storage options for shipment #1 due to the first shipment arriving prior to mobilization and the City's inability to secure storage.
 - Coordinate with Kompan transit team in Texas.
 - Arrange City-required "No Parking" sign placement along with delineations with the Contractor.
 - Review Contractor cost proposals.
- Facilitating play equipment delivery – shipment #2:
- Continual coordination and communication between the City, Kompan, and Ardurra included, but not limited to the following:
 - Coordinate with Kompan transit team in Texas for equipment delivery of shipment.
 - Arrange City-required "No Parking" sign placement along with delineations with the Contractor.
 - Work with MB Unified School District and MB Middle School for identification of safety issues related to the delivery; assisted superintendent with draft parent notification.
 - Schedule, cancel, and reschedule delivery due to the playground redesign #2.

On July 12, 2022, the Contractor demobilized due to time required to complete the redesign of the playground layout to address the conflicts between the play equipment footings and shade sail foundations and the shallow sewer line. Ardurra's efforts continued during the demobilization period.

Additional coordination, communication, and meeting efforts between the City, Engineer of Record, Contractor, Kompan, and Ardurra for the redesign of the playground layout due to the discovery of an unmarked/unidentified concrete slab and shallow sewer main included, but not limited to:

- 1st Redesign of playground:
 - Discuss identified conflicts between the play equipment footings and shade sail foundations and the concrete slab and sewer main.
 - Review of revised layout for compatibility and completeness to identify potential issues before issuance of revised plans.
 - Review of the revised resilient PIP surface for design, color layout, and quantities.
 - Coordinate revised shade sail structure re-engineered plans.
 - Coordinate a revised rendering of the redesigned playground layout from Kompan and conducted follow-ups with them for the City's publication.

Ardurra followed up with Kompan on August 30, 2022, regarding the revised rendering in which Kompan informed City staff and Ardurra about the change in the shipped Birdwatch Tower Slide dimension that significantly increased in length (approximately 6 to 8 feet) resulting in compliance and safety conflicts with the revision #1, which necessitated a redesign #2.

- 2nd Redesign of playground:
 - Discuss identified conflicts between the play equipment and fall zones.
 - Review of revised layout for compatibility and completeness to identify potential issues before issuance of revised plans.
 - Review of the revised resilient PIP surface for design, color layout, and quantities.
 - Coordinate confirmation that revised shade sail structure reengineered-engineered plans are not required.
 - Work with the play equipment vendor to obtain verification of structural reengineering approval from their overseas team regarding the redesign.
 - Follow-up with the play equipment vendor to obtain City-required written approval of redesigns in compliance with fall zones and engineering requirements.
 - Coordinate a revised rendering of the redesigned playground layout from Kompan.
- Coordination / review of additional PCOs related to the redesign.
 - Demobilization / remobilization.
 - Play equipment offloading.
 - Shade sail structure reengineering.
 - Re-survey of all construction staking.
 - Additional re-grading and reforming of the proposed concrete curb of the park footprint.
 - City-requested protective concrete slab extension over sewer line.

-
- Resilient PIP surface – additional quantities as a result of new park layout and footprint.
- City requested Ardurra to engage a firm for CPSI Playground Inspection services as required by California law:
 - This service was not included in the City’s RFP or as part of Ardurra’s original proposed scope of work.
 - Coordinate with CPSI firm to thoroughly identify the additional services to ensure compliance relating to play equipment distances (fall zone compliance).
 - Proposed scope to include:
 - 1) Plan review and comments.
 - 2) Site inspections and reports (2 each).
 - 3) Pre-completion site visit and summary.
 - 4) Impact tests and reports (2 each).

The impacts on the project completion schedule and related construction management efforts were not anticipated in Ardurra’s proposed and contracted scope and fee. Ardurra has endeavored to mitigate the impacts on the CM budget by efficiently managing the available allocations in our fee and efficient use of our staff. However, at this time we anticipate the remaining balance in the contract budget for CM and inspection will not be sufficient to fund the estimated time required to complete the project. Accordingly, Ardurra respectfully requests an amendment to the contract to cover these additional costs.

Scope of Services/Staffing

Ardurra proposes to continue its CM and inspection services through the updated expected Project completion date. Our CM team has been involved with the project from its beginning stages and are very familiar with the issues and current progress and will provide continuity to maintain an integral role in navigating this project through its challenges.

Should you have any questions or require additional information, please contact me at (714) 458-0703 or ddemilia@ardurra.com or Omar Alameddine at (949) 533-3012 or ocalameddine@ardurra.com. We look forward to continuing our work with the City on this important project.

Respectfully
submitted, Ardurra
Group, Inc.



Dino D’Emilia, PE. F. ASCE, QSD
California Public Works Practice Director
Management Services



Omar Alameddine
Group Leader, Project/Construction

**EXHIBIT B
APPROVED FEE SCHEDULE**

Ardurra's estimated fee was prepared based on the understanding that the Contractor has 79 working days remaining to complete the project with a projected additional 5 working days for extra work/rework for previously installed improvements due to the redesign. In addition, the fee also includes a construction contingency allowance should the completion date extend beyond the anticipated February 6, 2023 date. **ESTIMATED FEE**

**First Amendment Request for Extended Professional CM and Inspection Services for the
Polliwog Park Lower Playground Replacement Project
City of Manhattan Beach**

Current Contract Status				
Original Contract Amount				\$ 294,100.00
Amendments to Date				\$ -
Current Contract Amount				\$ 294,100.00
Billed to Date (<i>Through 8/31/2022</i>)				\$ 161,713.18
Current Contract Balance				\$ 132,386.82
Remaining Construction Period (estimate) 84 Working Days (October 3, 2022 to February 6, 2023)				
TITLE	Est. Hours Per Day	Total Hours	Hourly Rate	Extended Fee
Principal-in-charge	0.00	0.00	\$ 230.00	\$ -
Construction Manager	2.00	168.00	\$ 200.00	\$ 33,600.00
Public Works Inspector (<i>Prevailing Wage</i>)	8.00	672.00	\$ 145.00	\$ 97,440.00
Project Controls Engineer	4.00	336.00	\$ 135.00	\$ 45,360.00
Subtotal Remaining Fee				\$ 176,400.00
Remaining Post-Construction Period 10 Working Days				
TITLE	Est. Hours Per Day	Total Hours	Hourly Rate	Extended Fee
Principal-in-charge	0.00	0.00	\$ 230.00	\$ -
Construction Manager	2.00	20.00	\$ 200.00	\$ 4,000.00
Public Works Inspector (<i>Prevailing Wage</i>)	4.00	40.00	\$ 145.00	\$ 5,800.00
Project Controls Engineer	4.00	40.00	\$ 135.00	\$ 5,400.00
Subtotal Remaining Fee				\$ 15,200.00
Geotechnical, Materials Testing and Special Inspection (Geo-Advantech, Inc.)				\$ 22,350.00
Procure License Fee				\$ 3,435.00
Miscellaneous ODCs (Allowance)				\$ 8,000.00
CPSI Inspection (Allowance)				\$ 5,000.00
Subtotal Remaining Fee				\$ 38,785.00

Contingency Construction Phase		26 Working Days		
TITLE	Est. Hours Per Day	Total Hours	Hourly Rate	Extended Fee
Principal-in-charge	0.00	0.00	\$ 2 30.00	\$ -
Construction Manager	2.00	52.00	\$ 200.00	\$ 10,400.00
Public Works Inspector (Prevailing Wage)	8.00	208.00	\$ 145.00	\$ 30,160.00
Project Controls Engineer	4.00	104.00	\$ 135.00	\$ 14,040.00
Subtotal Contingency Allowance				\$ 54,600.00
Additional Requested Services				
Requested Amendment Amount				\$ 152,598.18

Terms and Conditions: Subject to the Agreement for Consulting Services between the City of Manhattan Beach and Ardurra Group, Inc., dated October 19, 2021.

AMENDMENT NO. 2 TO THE PROFESSIONAL SERVICES AGREEMENT
BETWEEN THE CITY OF MANHATTAN BEACH AND ARDURRA GROUP, INC.

This Second Amendment (“Amendment No. 2”) to that certain agreement by and between the City of Manhattan Beach, a California municipal corporation (“City”) and Ardurra Group, Inc., a Florida corporation (“Consultant”) (collectively, the “Parties”) is hereby made effective as of the date of the last authorized representative signature below (“Effective Date”).

RECITALS

A. On October 19, 2021, the City and Consultant entered into an agreement for professional services for the Consultant to provide inspection and construction management services for the Polliwog Park Lower Playground Replacement Project (“Agreement”).

B. On December 21, 2022, the City and Consultant entered into Amendment No. 1 to increase the Maximum Compensation by \$152,598.18 and modify the Scope of Services and Approved Fee Schedule approved by City Council. The Original Agreement, as amended by Amendment No. 1, is referred to herein as the “Agreement”.

C. The Parties now desire to amend the Agreement to modify the Scope of Services and Approved Fee Schedule.

NOW, THEREFORE, in consideration of the Parties’ performance of the promises, covenants, and conditions stated herein, the Parties hereby agree as follows:

Section 1. Section 3.A of the Agreement is hereby revised to increase the Maximum Compensation amount by \$49,856.50, for a new Maximum Compensation of \$496,554.68.

Section 2. Exhibit A (“Scope of Services”) of the Agreement is hereby amended to add the attached Exhibit A of this Amendment No. 2.

Section 3. Exhibit B (“Approved Fee Schedule”) of the Agreement is hereby amended to add the attached Exhibit B of this Amendment No. 2.

Section 4. Except as specifically amended by this Amendment No. 2, all other provisions of the Agreement shall remain in full force and effect.

[SIGNATURE PAGE FOLLOWS]

IN WITNESS THEREOF, the Parties hereto have executed this Amendment No. 2 on the day and year first shown above.

City:

Consultant:

City of Manhattan Beach,
a California municipal corporation

Ardurra Group, Inc.,
a Florida corporation

DocuSigned by:
Erick Lee, Acting City Manager
By: _____
Name: Bruce Moe 8/18/2023
Title: City Manager

DocuSigned by:
Lisa M. Penna, Vice President Regional Director
By: _____
Name: Lisa Penna, PE 8/16/2023
Title: Vice President, Regional Director

ATTEST:

DocuSigned by:
Liza Tamura
By: _____
Name: Liza Tamura 8/21/2023
Title: City Clerk

DocuSigned by:
Cathy Cahill, CFO
By: _____
Name: Cathy Cahill 8/16/2023
Title: Chief Financial Officer

APPROVED AS TO FORM:

DocuSigned by:
Quinn M. Barrow, City Attorney
By: _____
Name: Quinn M. Barrow 8/17/2023
Title: City Attorney

APPROVED AS TO FISCAL IMPACT:

DocuSigned by:
Julie Bondarchuk
By: _____
Name: Julie Bondarchuk 8/16/2023
Title: Acting Finance Director

APPROVED AS TO CONTENT:

DocuSigned by:
Erick Lee
By: _____
Name: Erick Lee 8/16/2023
Title: Public Works Director

EXHIBIT A SCOPE OF SERVICES

Pursuant to discussions during the June 2, 2023 meeting with the Parties, several unforeseen issues require additional efforts to resolve and are resulting in delays to project completion, as further detailed below.

• **Unforeseen, shallow mainline sewer and above ground maintenance structure.** An undocumented 16-inch-diameter sewer mainline with only 6 inches of cover was discovered in conflict with the proposed playground and shade structure components. This mainline was also discovered to be connected to an above-grade brick maintenance structure that was decorated as the existing lighthouse feature of the playground area. AGI was directed by the City to implement the necessary additional services to assist with resolving this issue as follows:

- Original direction by the City to reconstruct the maintenance structure.
 - Numerous discussions, meetings, calls, and correspondence with City Engineer, City project manager, Prime contractor (LSS), City-identified sewer contractor (Doreck) regarding the reconstruction.
 - Facilitate, discuss, and negotiate scope of work with Doreck, which included but was not limited to numerous calls and meetings and cost proposal reviews and revisions.
 - Coordinate and facilitate with LSS to engage Doreck as subcontractor, submit change order request, and coordination of field activities to allow the work to be completed.
 - Additional inspections required for all Doreck-related work.

- Change in direction from the City to abandon the maintenance hole.
 - Coordinate new direction with Doreck, contractor, and City project manager.
 - Review sewer tie-in options with City staff and Doreck.
 - Advise on scope and review of Change Order Request (COR) revisions.
 - Numerous meetings, site visits, and correspondence with City Engineer, City project manager, LSS, Doreck regarding tie-in process.
 - Inspect services for pre and post tie-in operations.

• **Coordinating “Robinia” wood play equipment remediation to address safety and aesthetic concerns.**

- Obtain maintenance information regarding play equipment.
- Coordinate and schedule wood repairs/maintenance prior to playground opening.

• **Administer and document general contractor demobilizations due to weather conditions and unforeseen sewer line issue.**

- **Biweekly progress meetings facilitated throughout the extended construction period and various demobilizations.**

- **Play equipment footing detail discrepancies as a result of Request for Information (RFI) #17 response.**
 - Review of the revised footing details issued as part of the RFI response.
 - Discuss identified conflicts between the play equipment footing details with City, SWA / Huitt-Zollars, Sadler, and Kompan.
 - Site meetings and additional verification efforts to resolve the issue related to the footings.

- **Coordination, communication, and meetings** between the City, Engineer of Record, Contractor, and Kompan to address designer's and play structure manufacturer's conflicting RFI responses, and to identify a feasible solution.

- **Additional coordination and tracking efforts** with the equipment vendor, Kompan, for missing play equipment parts.

**EXHIBIT B
APPROVED FEE SCHEDULE**

ESTIMATED FEE				
Second Amendment Request for Extended Professional CM and Inspection Services for the Polliwog Park Lower Playground Replacement Project City of Manhattan Beach				
Current Contract Status				
Original Contract Amount				\$ 294,100.00
Amendments to Date				\$ 152,598.18
Current Contract Amount				\$ 446,698.18
Billed to Date (Through 5/31/2023)				\$ 430,426.32
Current Contract Balance				\$ 16,271.86
Remaining Construction Period (estimate)		22 Working Days (June 1, 2023 to June 30, 2023)		
TITLE	Est. Hours Per Day	Total Hours	Hourly Rate	Extended Fee
Principal-in-charge	0.00	0.00	\$ 230.00	-
Construction Manager	1.00	22.00	\$ 200.00	4,400.00
Public Works Inspector (Prevailing Wage)	4.00	88.00	\$ 145.00	12,760.00
Project Controls Engineer	4.00	88.00	\$ 135.00	11,880.00
Subtotal Remaining Fee				\$ 29,040.00
Remaining Post-Construction Period		5 Working Days		
TITLE	Est. Hours Per Day	Total Hours	Hourly Rate	Extended Fee
Principal-in-charge	0.00	0.00	\$ 230.00	-
Construction Manager	1.00	5.00	\$ 200.00	1,000.00
Public Works Inspector (Prevailing Wage)	4.00	20.00	\$ 145.00	2,900.00
Project Controls Engineer	2.00	10.00	\$ 135.00	1,350.00
Subtotal Remaining Fee				\$ 5,250.00
Geotechnical, Materials Testing and Special Inspection (Geo-Advantec, Inc.)				\$ 17,429.44
Procore License Fee				\$ 2,651.90
Miscellaneous ODCs (Allowance)				\$ 7,792.02
CPSI Inspection (Allowance)				\$ 3,965.00
Subtotal Remaining Fee				\$ 31,838.36
Requested Amendment Amount				\$ 49,856.50
